

BUILD PLAN · OCTOBER 2026

# From website to *live marketplace.*

What is built, what comes next, and what the founder needs to set in motion, for the Abhiyantri Setu customer app, partner app, admin and vendor portals and backend.


| | |
|---|---|
| 1. Where things stand | 2 |
| 2. Step 0: this week | 3 |
| 3. Approvals only the founder can start | 3 |
| 4. Timeline | 5 |
| 5. Phase 1: core loop | 6 |
| 6. Phase 2: trust and projects | 7 |
| 7. Phase 3: supply and scale | 7 |
| 8. Team and running costs | 8 |
| 9. Risks and launch checklist | 9 |



**Abhiyantri Setu** · Greater Noida

Prepared for Vivek Shukla · 18 October 2026

Repository: silentknight-sudo/abhiyantrisetu_fullstack

1 · STATUS

# Where things *stand.*

Phase 0 (Foundation) from the architecture document is complete, and the public website is built and ready to deploy in pre-launch mode. The transaction loop, mobile apps and portals are not started yet.

**63** automated tests passing

**21** core database tables

**81** website pages generated

**72** local SEO pages (service × sector)

| Area | What exists | Status |
|---|---|---|
| Monorepo and shared code | Turborepo + pnpm; shared design tokens (navy, orange, sand), business rules (job states, GST, money in paise, phone checks) and validation used by every surface | Done |
| Backend API (NestJS) | Postgres + PostGIS schema with migrations; unified requirements table for service, renovation, materials, equipment and consults | Done |
| Phone OTP login | MSG91 adapter, hashed codes, cooldowns and attempt limits, rotating sessions, partner device binding, in-app account deletion | Done |
| Job state machine | The hire event; hired → scheduled → in progress → completed → closed, with cancel and dispute; 4-digit start codes; 48-hour auto-confirm worker | Done |
| Website (Next.js) | Warm cream theme, 3D bridge hero (providers ↔ clients), 3D house tracker, scroll animations, cost calculator, FAQ, SEO pages; “Coming soon” pre-launch mode with one switch to go live | Done |
| CI | Formatting, build, type checks, tests against PostGIS, schema-drift check on every push | Done |
| Matching, quotes, payments | Not started | Phase 1 |
| Customer and partner apps | Not started (Expo, one codebase, two store listings) | Phase 1 |
| Admin and vendor portals | Not started | Phase 1 / 3 |
| Data from Lovable / Supabase | Needs access to the current Supabase project or a schema export | Needs you |

2 · IMMEDIATE

# Step 0: *this week.*

Make the Coming-soon website useful from day one: it should collect real demand while the app is being built.

| Task | Owner | Why it matters |
|---|---|---|
| Deploy the website to Vercel (Root Directory `apps/web`) and connect the domain | You · 5 min | Puts the brand online; settings are in the README |
| Replace placeholders: WhatsApp number, phone, emails, prices, example society name (`apps/web/src/lib/content.ts`) | You | "Notify me on WhatsApp" currently reaches nobody |
| Early-access sign-ups: waitlist API storing name, phone, sector and service, with an export | Dev · ~1 day | Builds the first list of customers and partners before launch |
| Product analytics (PostHog) on the website | Dev · ½ day | Shows which sectors and services people want first |
| Deploy the API to AWS Mumbai (ap-south-1) with managed Postgres | Dev after AWS account | Needed for the waitlist and everything after it; keeps data in India (DPDP) |

3 · FOUNDER ACTIONS

# Approvals only *you can start.*

These take weeks to clear and block the launch, so start them now, in parallel with development.


| Item | Typical lead time | Unblocks |
|---|---|---|
| **DLT registration** for SMS: entity, sender header, OTP template, via MSG91 | 1–2 weeks | Real OTP login |
| **WhatsApp Business API** through a provider (Interakt, AiSensy or Gupshup) and message-template approval | 1–2 weeks | Lead alerts with Accept buttons for partners |
| **Razorpay** account and KYC, plus **Route** for split and on-hold transfers; RazorpayX for payouts | 1–3 weeks | Payments, Setu Safe, weekly partner payouts |
| **Apple Developer** (organisation needs a D-U-N-S number) and **Google Play Console** | 1–3 weeks | App Store and Play Store listings |

| Item | Typical lead time | Unblocks |
|---|---|---|
| **KYC provider** contract (IDfy or Surepass): Aadhaar via DigiLocker, PAN, face match, bank check | 1–2 weeks | Partner verification |
| **Legal:** terms, DPDP privacy notice (English and Hindi), named grievance officer, lawyer sign-off on Setu Safe wording (RBI rules on holding money) | 2–4 weeks | Launch compliance and store approval |
| **AWS account** (Mumbai region), domain DNS on Cloudflare | 1 day | Hosting the API |
| **Supabase access** or schema and data export from the Lovable app | — | Migrating existing users and data |

4 · TIMELINE

# Twenty-six weeks *to scale.*

Indicative dates, assuming work starts Monday 19 October 2026 with the team in section 8. Do not start Phase 2 until one real requirement has gone end to end on the new system.

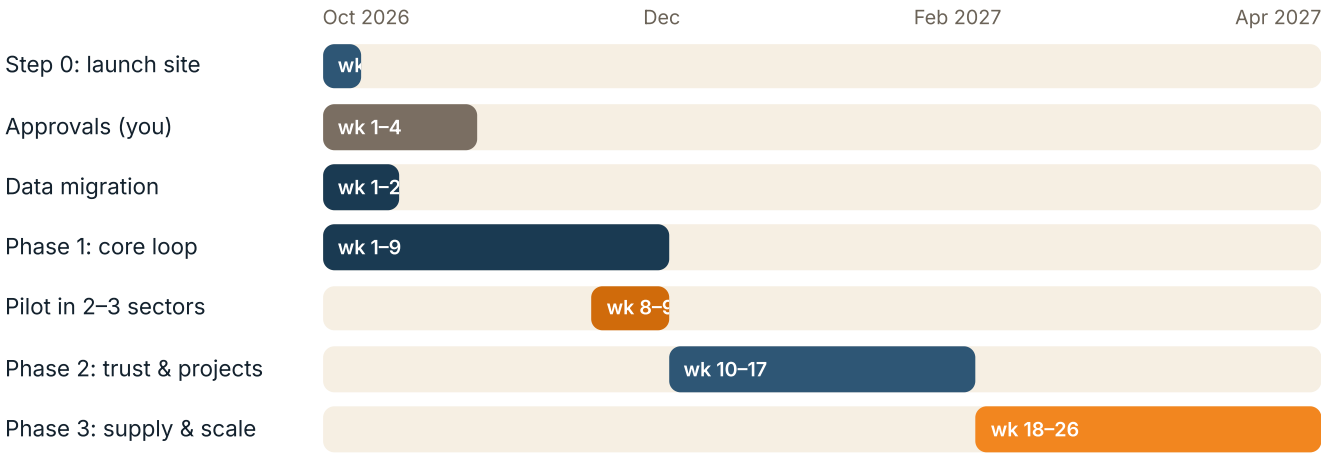


| Phase | Dates (indicative) | Gate to move on |
|---|---|---|
| Step 0 | 19–25 Oct 2026 | Website live, waitlist collecting sign-ups |
| Phase 1 · Core loop | 19 Oct – 20 Dec 2026 | One real Greater Noida job completed and reviewed end to end; website switched from Coming soon to live |
| Phase 2 · Trust and projects | 21 Dec 2026 – 14 Feb 2027 | Share of requirements with 2+ quotes in 24 hours tracked weekly and rising |
| Phase 3 · Supply and scale | 15 Feb – 18 Apr 2027 | Core loop stable; ready for the next city |

**North-star metric:** the share of posted requirements that receive two or more quotes within 24 hours. It measures supply, matching and partner responsiveness together, and is what customers feel first.

5 · PHASE 1 · WEEKS 1–9

# The core *loop.*

Goal: a customer posts a requirement, verified pros quote, the customer hires, work starts with the start code, gets paid for and reviewed, entirely on the new system.

## Backend modules

| Module | Scope |
|---|---|
| Data migration | Move users, partners and requirements from Lovable/Supabase; verify counts and spot-check before cut-over |
| Catalog and pricing | Categories, services, variants and base prices; drives forms and SEO pages |
| Matching | Verified partners within a radius (PostGIS), ranked by distance, rating, response time and acceptance rate; rules first, learned ranking after about 5,000 jobs |
| Leads and credits | Fan-out to matched partners, seen and responded timestamps, lead credits and top-ups |
| Quotes and negotiation | Line items, optional GST, proposed milestones, counter-offers with revision history; accepting a quote creates the job (the hire event, already built) |
| Payments | Razorpay orders and signed, idempotent webhooks; append-only ledger |
| Notifications | WhatsApp leads with Accept buttons, push notifications, SMS fallback, quiet hours |
| API client | Typed client generated from the API spec, shared by apps and portals |

## Apps and portals

### Customer app · iOS + Android

Login, post a requirement (all five types), compare and negotiate quotes, hire, job tracking with start code, payment, review, profile and account deletion.

### Partner app · “Setu Partner”

Onboarding and KYC upload, lead inbox, quoting with GST, today’s jobs, enter start code, mark complete, earnings. Same Expo codebase, separate store listing.

### Admin portal v1

Partner verification queue, requirements and jobs, manual overrides with audit log, catalog editing. Behind Google sign-in.

### Pilot and launch

Onboard 30–50 partners in 2–3 sectors (Sector Pi, Alpha, Gamma), run real jobs, then set `NEXT_PUBLIC_LAUNCHED=true` to switch the website live.

6 · PHASE 2 · WEEKS 10–17

# Trust and *projects.*

| Feature | Scope |
|---|---|
| Project tracker | Milestones with photo proof and approval; daily site log |
| Setu Safe | Milestone payments held via Razorpay Route on-hold transfers and released on approval (wording signed off by a lawyer) |
| House construction tracker | The 10 stages on the website, with engineer inspections, visit reports and stage payments |
| Reviews and disputes | Verified-hire reviews and partner replies; dispute desk in admin; payouts frozen while disputed |
| Partner payouts | Weekly cycle via RazorpayX with bank-account validation; payout history in the partner app |
| Field-agent mode | Beat plans and on-site partner registration in the partner app |
| Setu AI v1 | Hinglish chat that drafts requirements and suggests services; photo diagnosis (seepage, cracks, wiring); estimates always marked indicative; nothing booked without the user's tap |

7 · PHASE 3 · WEEKS 18–26

# Supply and *scale.*

| Feature | Scope |
|---|---|
| Vendor portal | For suppliers, rental firms and larger contractors: RFQ inbox, BOQ line-item quoting, rate cards, inventory, GST invoices, team logins |
| Materials RFQ | BOQ upload (photo or Excel) turned into line items by AI; market-rate comparison; delivery scheduling |
| Equipment rental | JCBs, mixers, scaffolding; operator details; daily work log |
| Societies and RWAs | Organisation accounts, tower-wise progress, recurring maintenance visits, single point of contact |
| Hindi everywhere | Voice input and replies in Hindi and Hinglish; Hindi website pages; a content system for guides and city pages |
| Next city | Sector data, partner supply plan and local SEO pages for the next launch city |

8 · RESOURCES

# Team and *running costs.*

| Role | Count | Focus |
|---|---|---|
| Tech lead / architect | 1 | Architecture, API contracts, code review |
| Backend engineers (NestJS, Postgres) | 2 | Modules, payments, integrations |
| Mobile engineers (React Native / Expo) | 2 | Customer and partner apps |
| Web engineers (Next.js) | 2 | Website, admin and vendor portals |
| UI/UX designer | 1 | App screens in the existing identity |
| QA engineer | 1 | Testing on low-end Android phones |
| DevOps (part-time) | 0.5 | AWS, CI/CD, monitoring |
| Product owner | 1 | Founder or PM; scope and the north-star metric |

## Approximate monthly running cost at launch

| Item | Range (INR / month) |
|---|---|
| AWS (API servers, Redis, storage, data transfer) | 15,000 – 40,000 |
| Database (Supabase Pro or AWS RDS) | 2,500 – 15,000 |
| Vercel, Cloudflare, Sentry, PostHog | 5,000 – 15,000 |
| AI (Claude and Sarvam) at early volumes | 5,000 – 25,000 |
| WhatsApp, SMS, maps, KYC (usage-based) | 10,000 – 40,000 |
| Apple Developer + Google Play | ~8,500 per year + ~2,100 one-time |

Rough planning figures from typical early-stage usage, carried over from the architecture document, not quotes. Confirm each vendor’s current pricing before budgeting.

9 · RISKS AND LAUNCH

# Risks and the *launch checklist.*

| Risk | Mitigation |
|---|---|
| Approvals run late (DLT, WhatsApp, Razorpay, app stores) | Start them this week; build against sandboxes; keep the website in Coming-soon mode until they clear |
| Too few partners at launch | Use the waitlist and field agents to sign up partners in 2–3 sectors before opening to customers |
| Holding customer money (RBI rules) | Setu Safe built on Razorpay Route on-hold transfers; wording approved by a lawyer before launch |
| Slow on low-end Android phones | Test on real mid-range devices; 3D on the website already falls back to static art; keep app bundles lean |
| Data loss when leaving Lovable | Migrate to a copy first, verify counts and samples, then cut over |
| Wrong prices or promises on the site | Replace placeholder prices and confirm every “Why trust Setu” claim is true at launch |

## Launch checklist

- [ ] DLT templates approved; real OTP works on Jio, Airtel and Vi numbers
- [ ] WhatsApp templates approved; partners can accept a lead from WhatsApp
- [ ] Razorpay live keys; one real payment and refund tested; webhooks verified
- [ ] 30–50 verified partners in the launch sectors
- [ ] Terms, DPDP privacy notice (English and Hindi), grievance officer published
- [ ] Apps approved on App Store and Google Play (account deletion, Data Safety form, background-location justification)
- [ ] Monitoring live (Sentry, uptime checks); database backups and a tested restore
- [ ] One real job completed end to end and reviewed
- [ ] Website switched live: `NEXT_PUBLIC_LAUNCHED=true`, real WhatsApp number and prices

**Recommended next step:** build Step 0’s waitlist and analytics so the Coming-soon site collects leads from day one, then start the Phase 1 backend while the approvals come through.
